Sec. 11-95-13

COR. B | I.P. | 5-1-29 | Set I.P. | Set PK to New mat 7-26-05

Found 1½ ϕ Iron Rod 10-27-67 ReTied Found Stone & I.P. Stone had X

COR C | Stone | Chiseled on Top | Set I.P. on X ϕ | Retied 4-20-07

Set mag nail w/ steel washer File 2003-2391

COR. B | I.P. | Construction point set 10-30-67

17.0 Feet South of Sec. Cor

Reset PK after resurfacing 7-26-05

Consultant found PKs 8-29-05. File 2005-1874

COR B. | 1½ ϕ | Rod (North PIN Sec. Cor.)
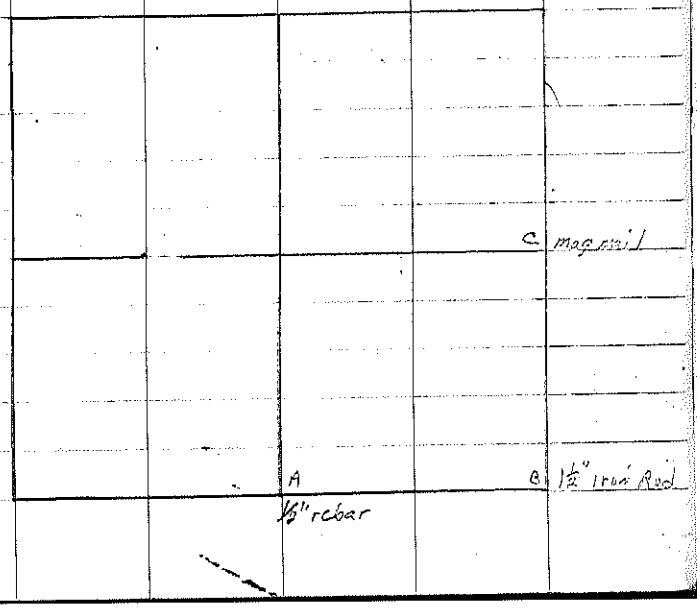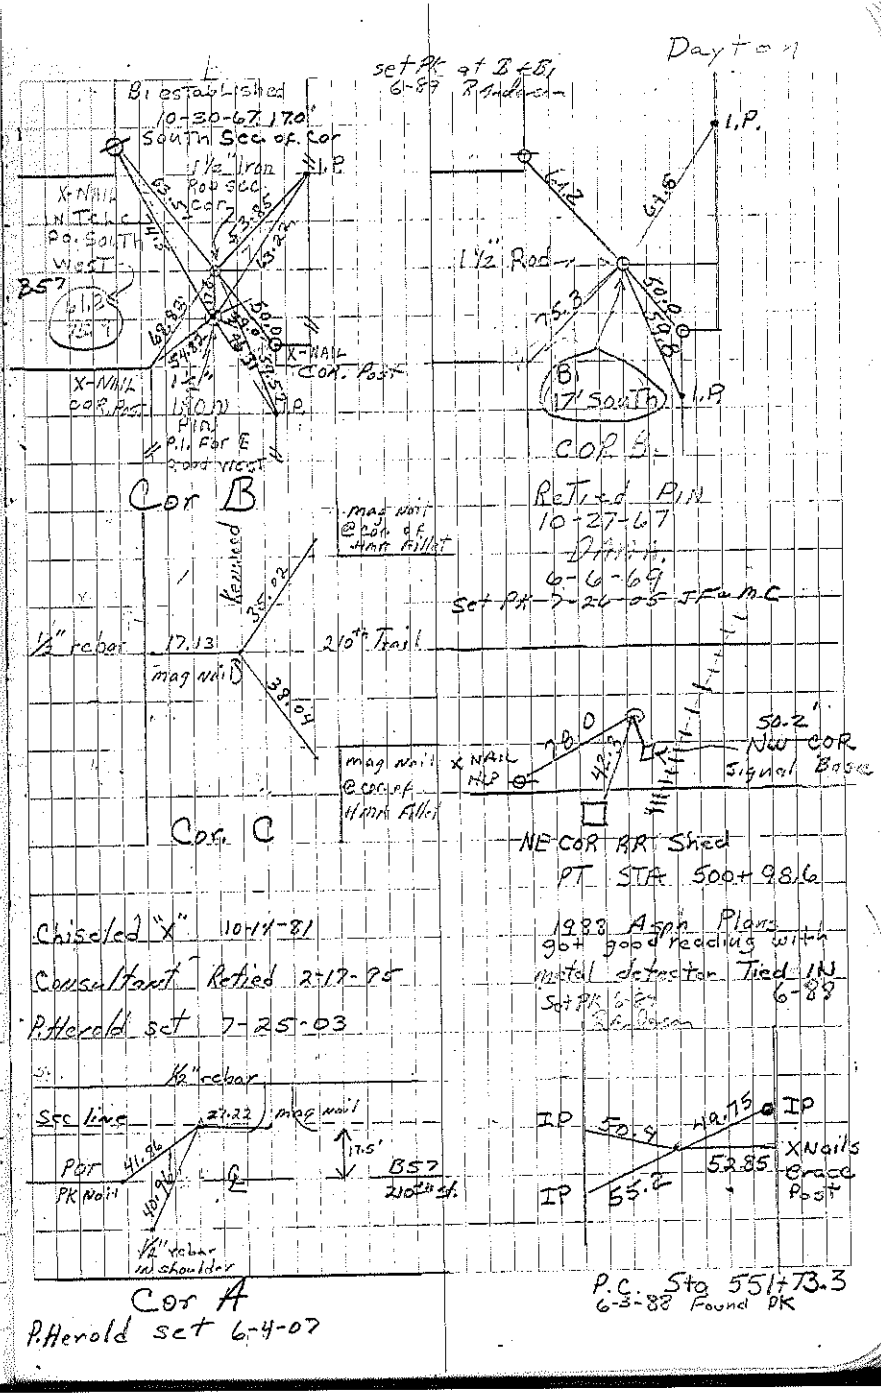
Cor. A | Set ½" rebar w/ 2" cap 6-4-07. File 2007-1187
